



CENTRAL TRI-STATE TOLLWAY (I-294) CONSTRUCTION UPDATE

Manar Nashif, *Chief Engineering Officer*
September 2024

CENTRAL TRI-STATE TOLLWAY PROJECT STATUS



\$3.2 billion

spent

\$4 billion project
budget

165

contracts awarded

70 contracts
closed out

95


active contracts

Design, construction,
inspection, other*





MAJOR HIGHLIGHTS

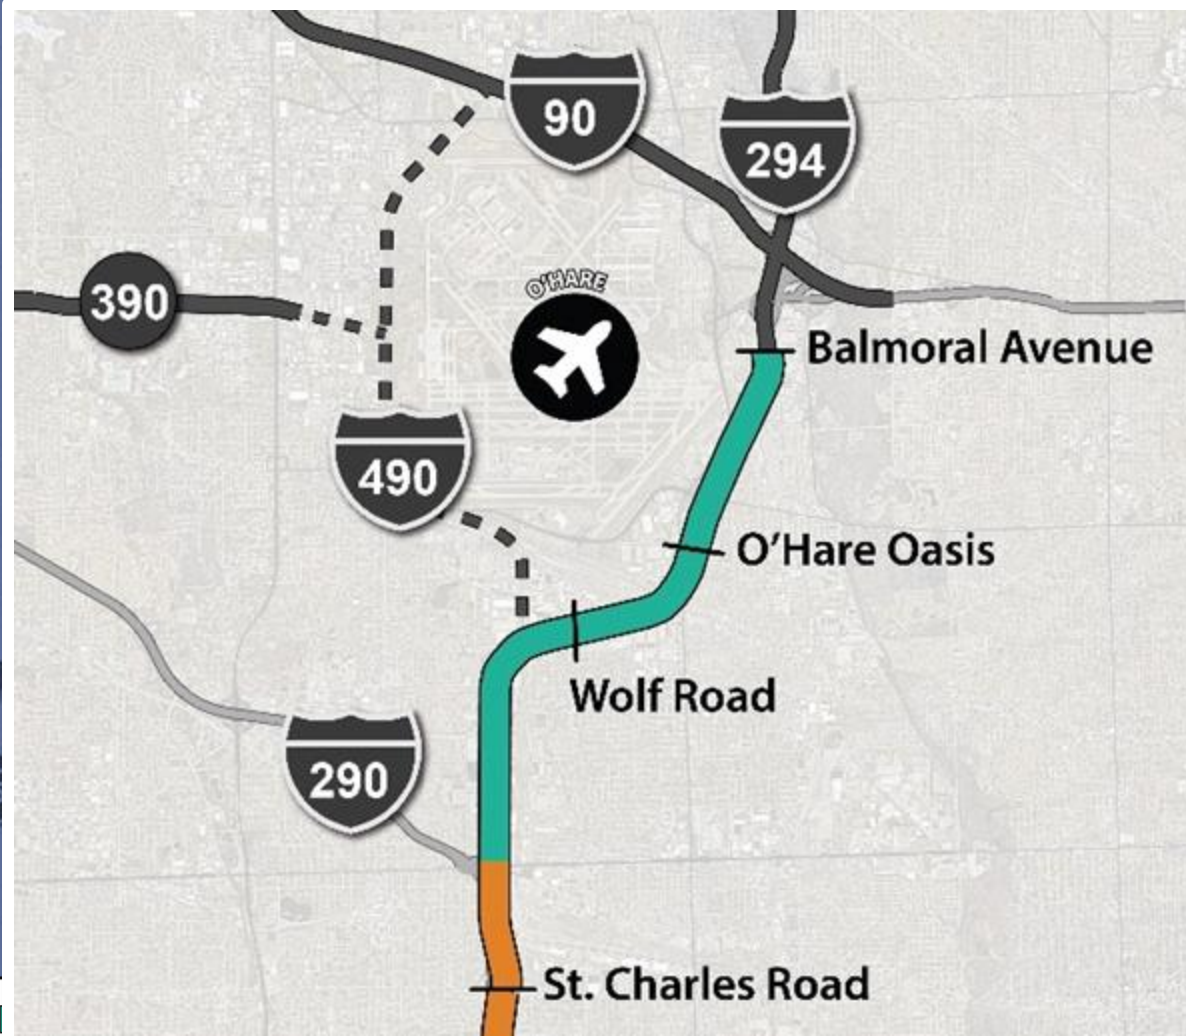


North section



WORK COMPLETED

Fifth lane open on SB I-294 between Irving Park Road and WB I-290

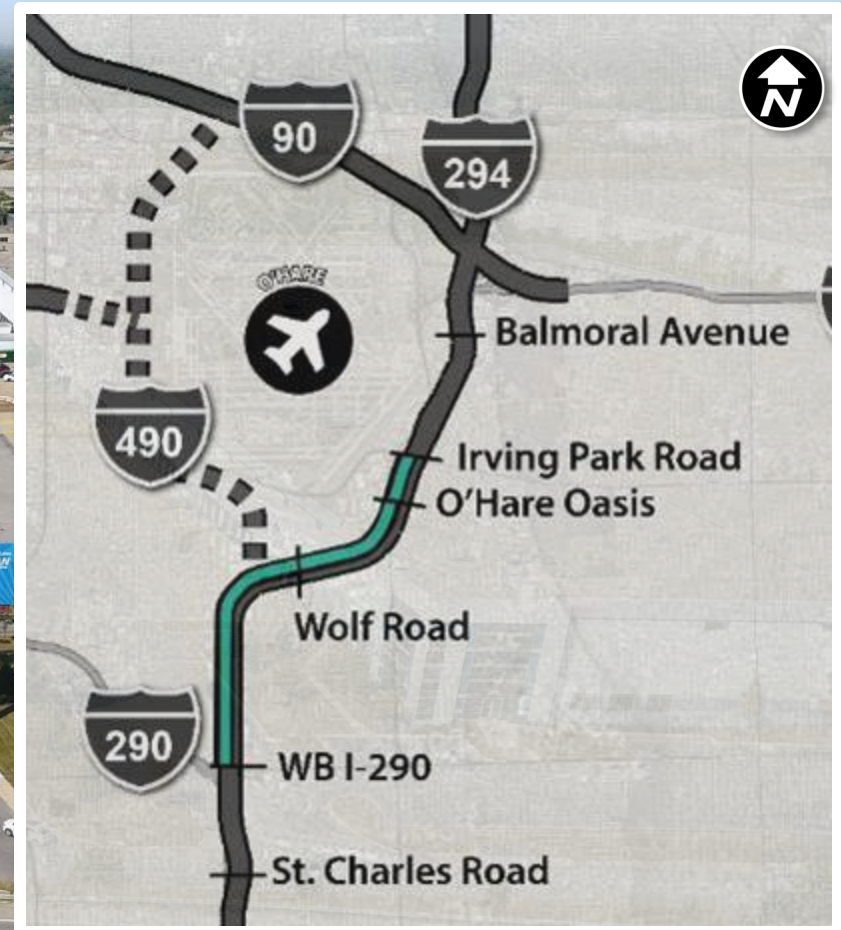

Fifth lane open on SB I-294 between Irving Park Road and WB I-290




ACTIVE TRAFFIC MANAGEMENT

14

SmartRoad gantries
installed between
Rosemont and Elmhurst



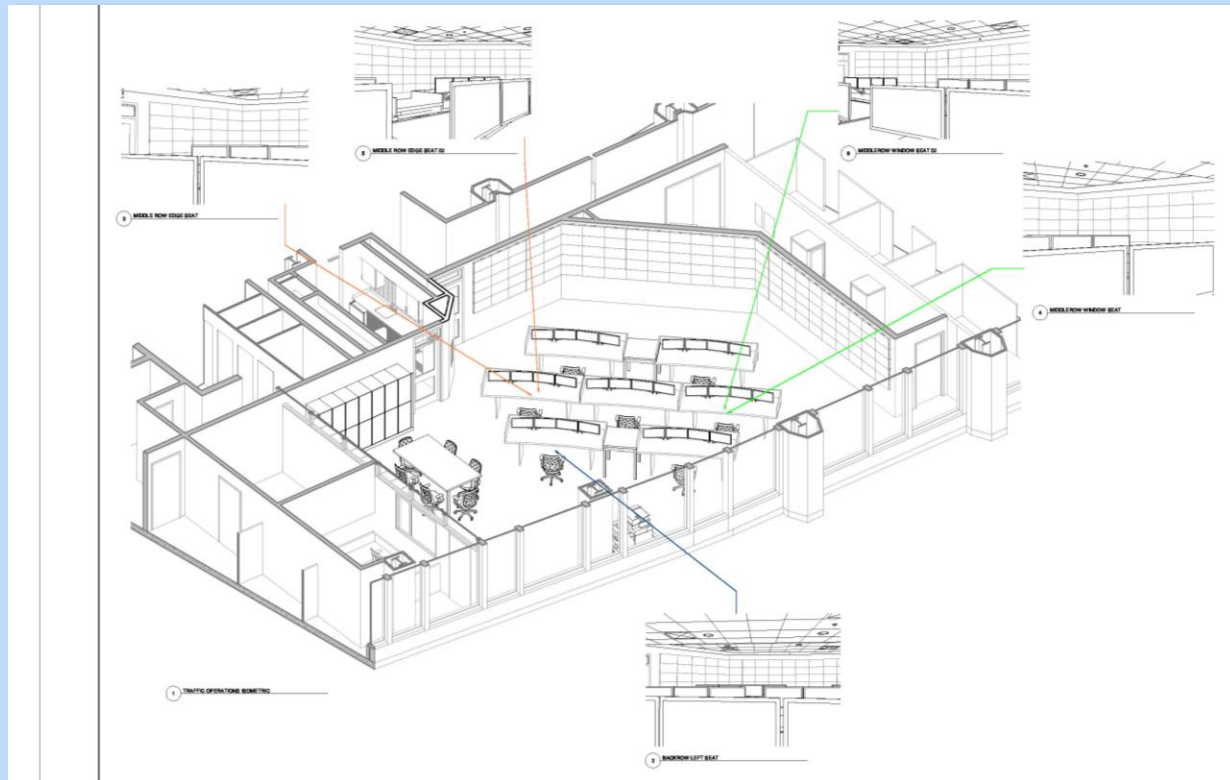

TRAFFIC OPERATIONS CENTER/ DISPATCH IMPROVEMENTS



I-490/I-294 INTERCHANGE PROJECT

33

miles of lane
paving

Nearly 15
million

pounds of
structural steel

Nearly
500,000

cubic yards of
grading



I-490/I-294 INTERCHANGE PROJECT



ECONOMIC DEVELOPMENT

City of Northlake


- New development along Northwest Avenue

City of Elmhurst

- New development along County Line Road

North Avenue Interchange

- Partnership with Cook County and Cities of Elmhurst and Northlake
- County Line Road ramp opening 2025

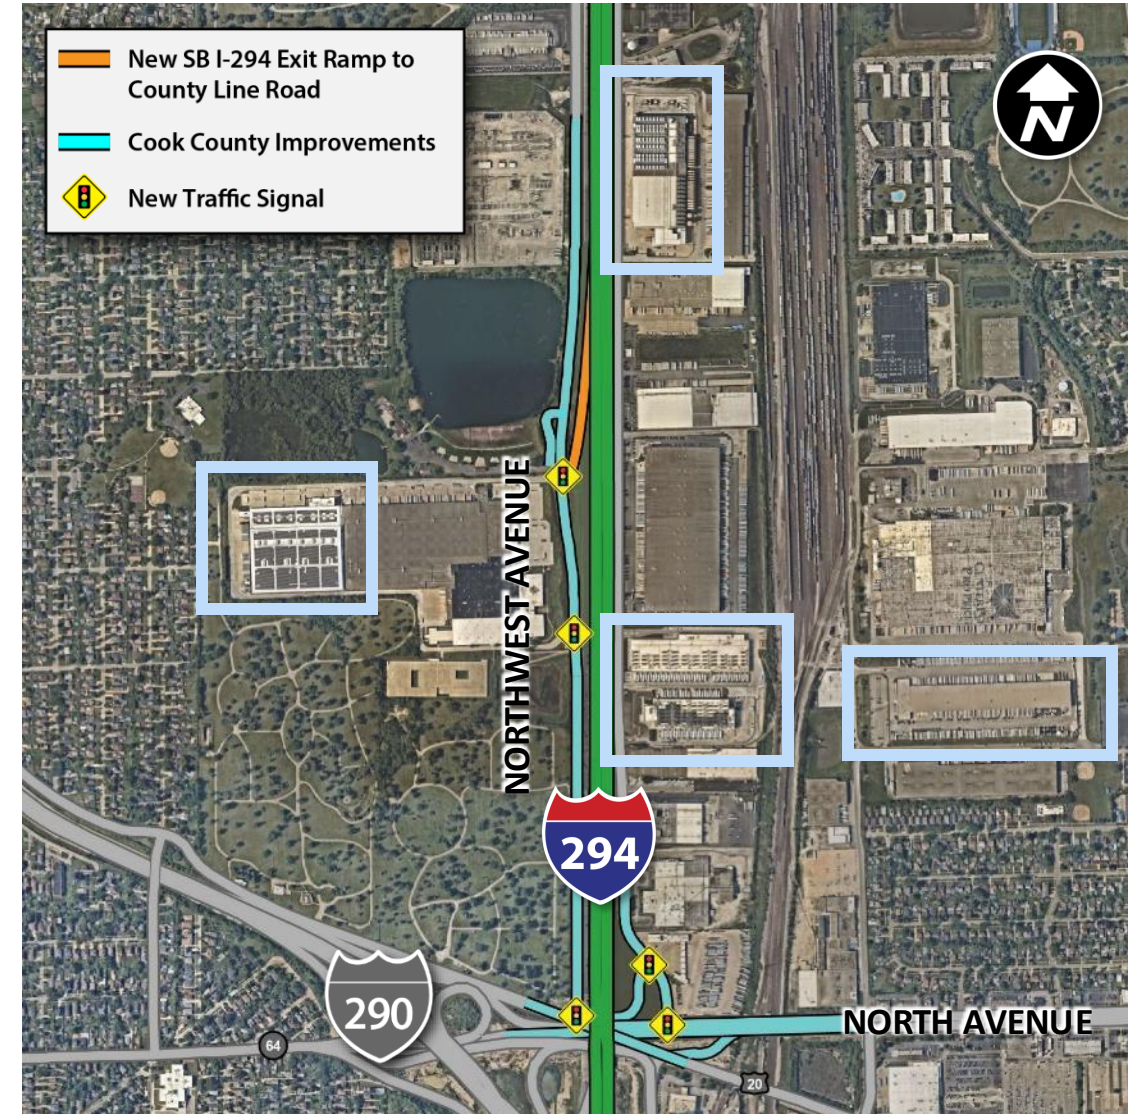



THANK YOU

Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290





CONSTRUCTION UPDATES

